

Kai Tak Sports Park


Progress Updates and Proposed Temporary Works Areas



Location




Indicative Master Layout Plan

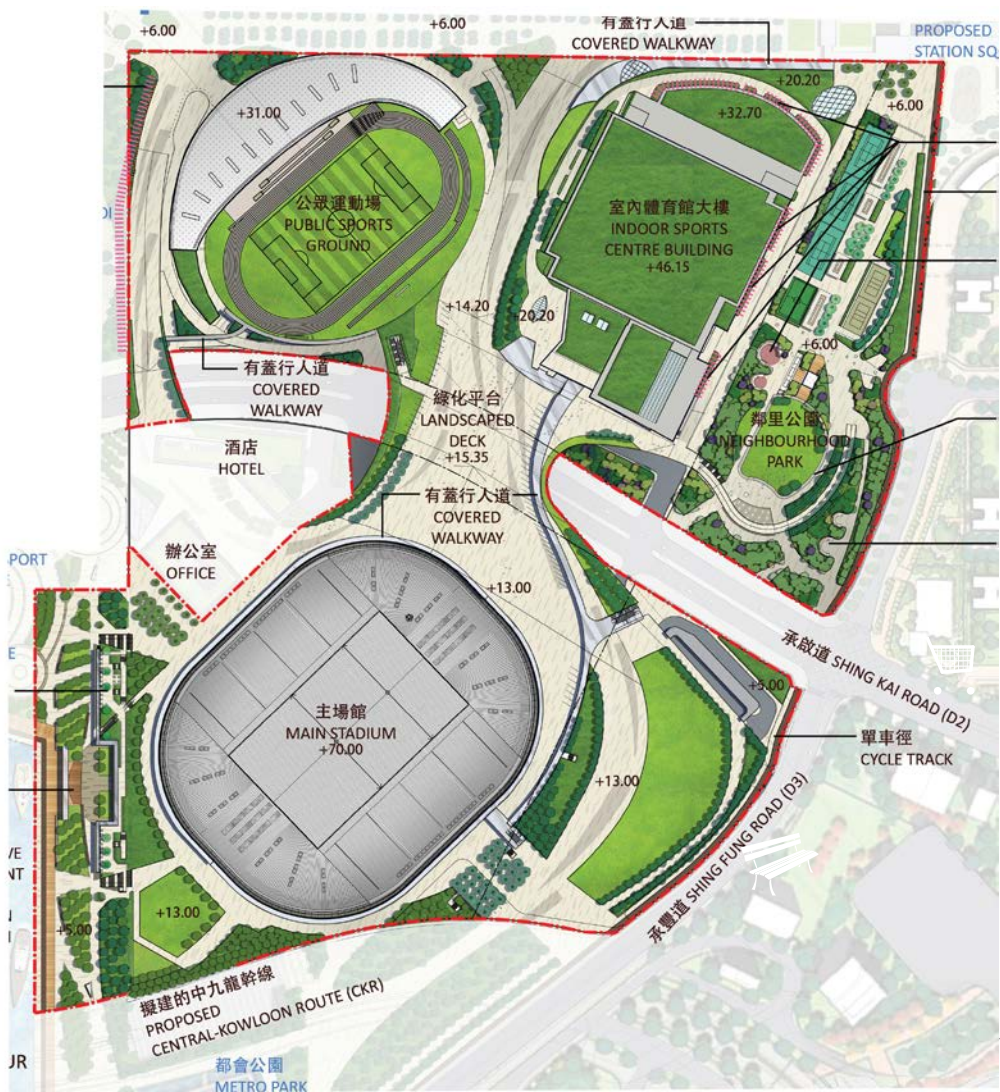

Progress

- The Environmental Protection Department approved the Environmental Impact Assessment (EIA) Report for the Sports Park project on 6 January 2017 and issued the Environmental Permit on 8 September 2017.
- LegCo approved the funding application of about **\$31.9 billion** (in M.O.D. price) in late June 2017 for the design and construction of the Sports Park
- Prequalification completed in Sep 2017 with 3 successful applicants selected. Tenders will be invited soon.


Tendering

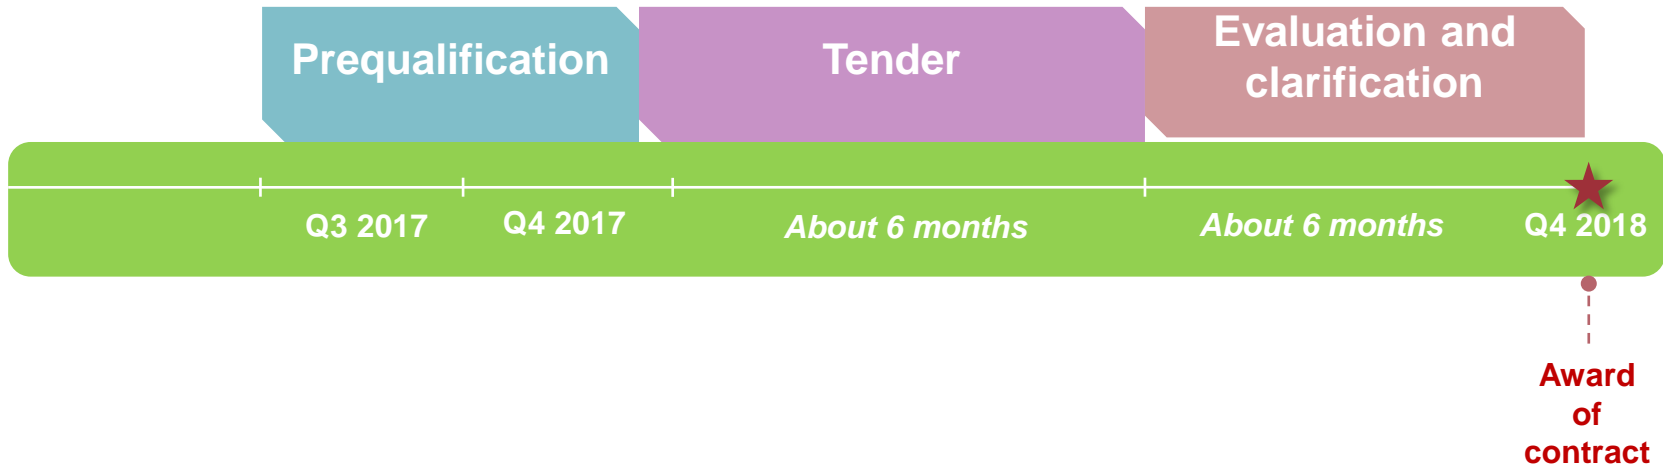


Assessment on tender proposals will be based on quality and price

Estimated completion date: 2022-2023


Proposed Temporary Works Areas

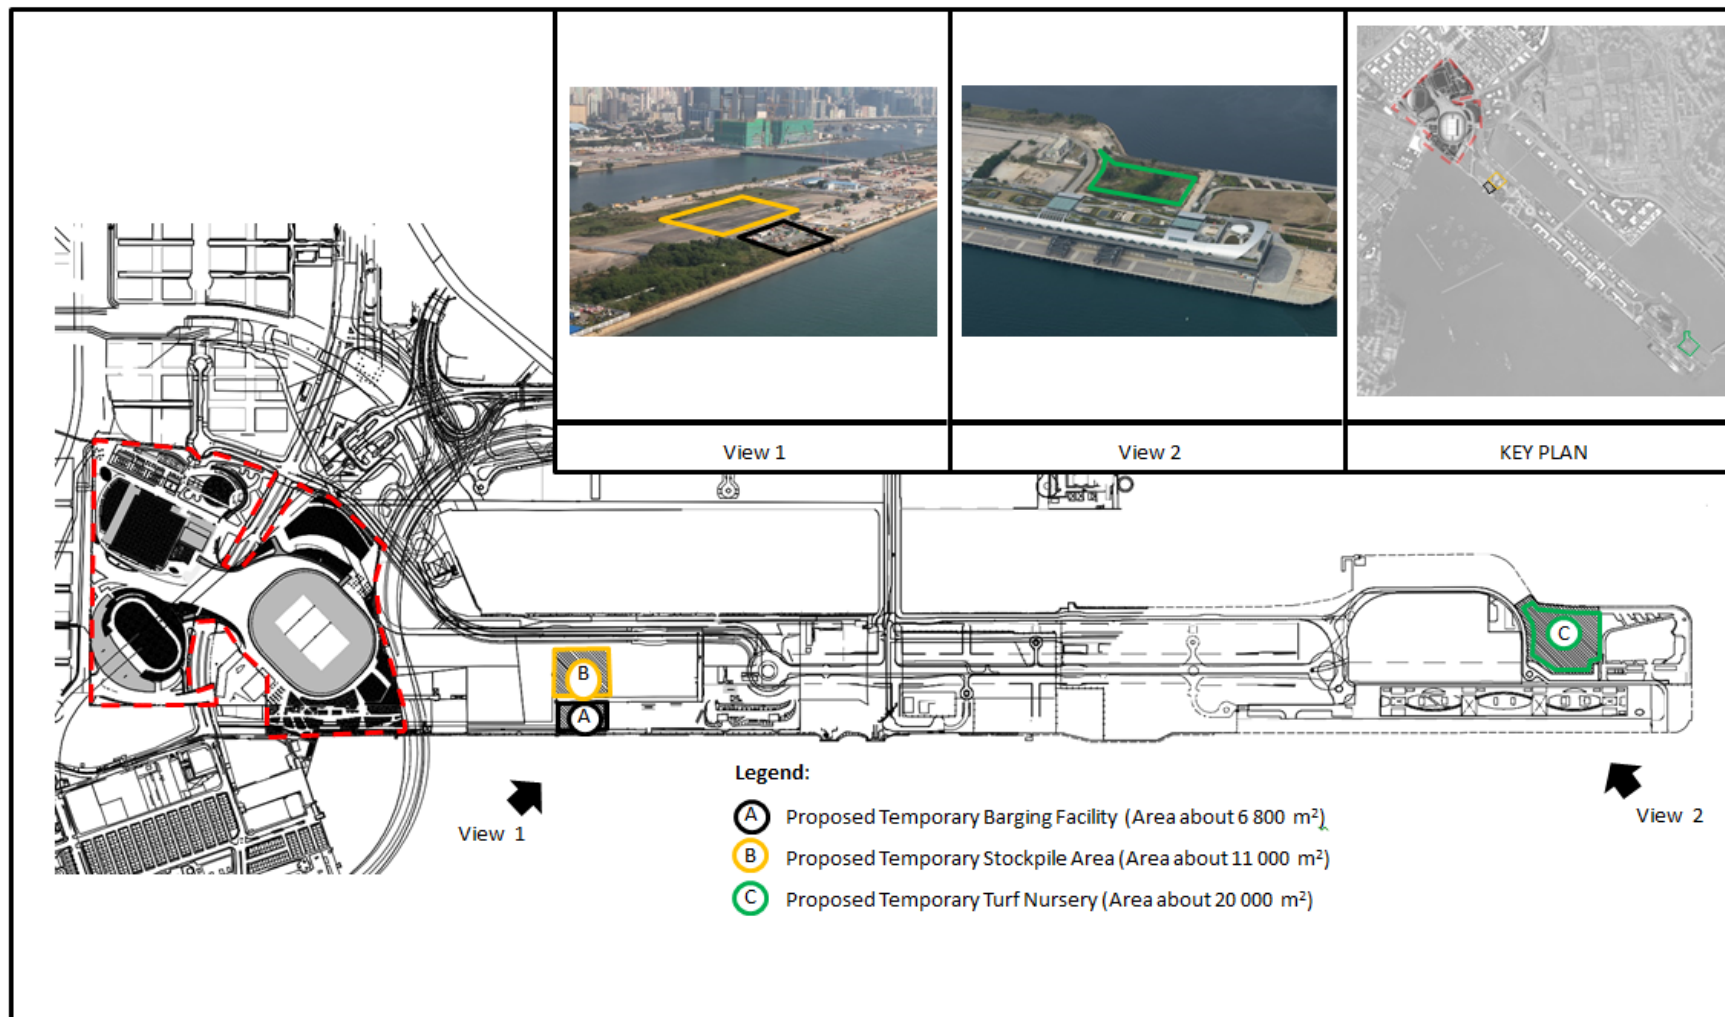

Proposed Temporary Works Areas

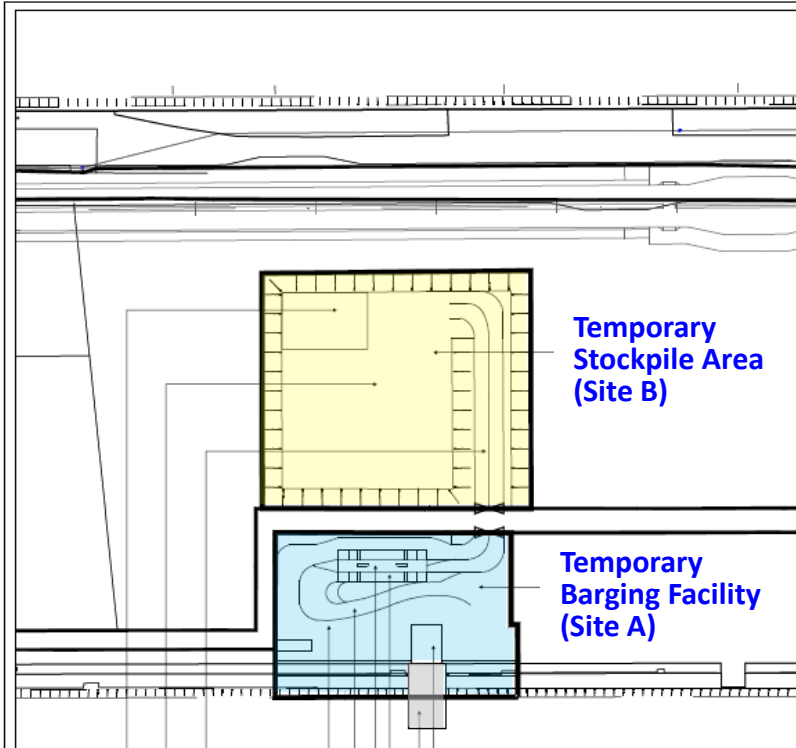


- Access Ramp
- Tipping Hall
- Weighbridge
- Recorder House
- Access Ramp
- Access Ramp
- Stockpile Area
- Sorting Facility

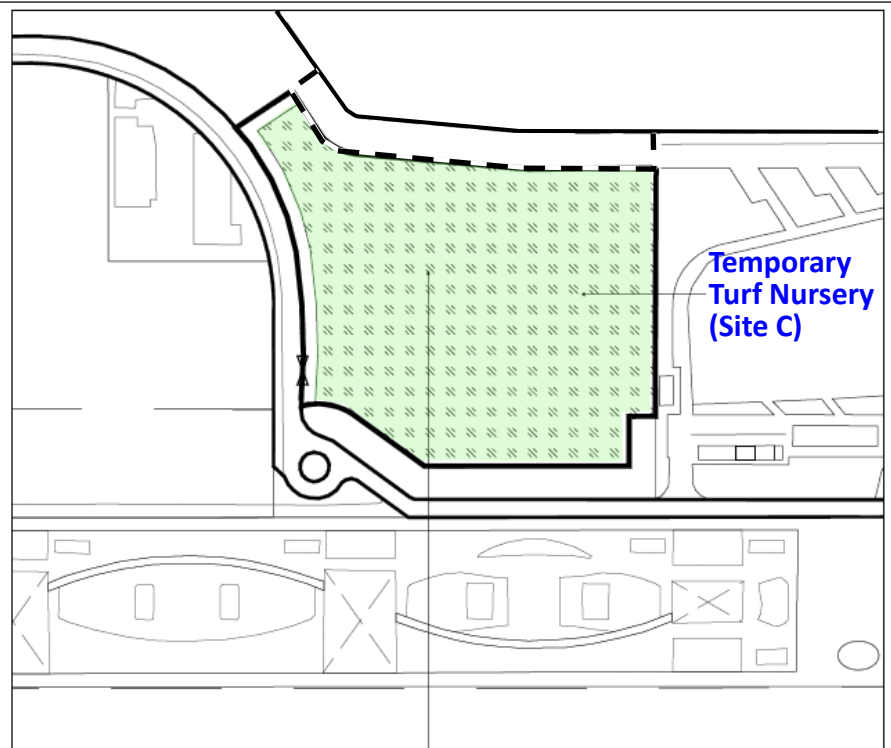

Pitch Area of Main Stadium (132 x 78 m)	=	10,296 m ²
<u>Pitch Area of Public Sports Ground (105 x 68 m)</u>	=	<u>7,140 m²</u>
Total Pitch Area	=	17,436 m ²
Total Turf Area in Nursery	=	17,510 m ²

Land Requirement Plan

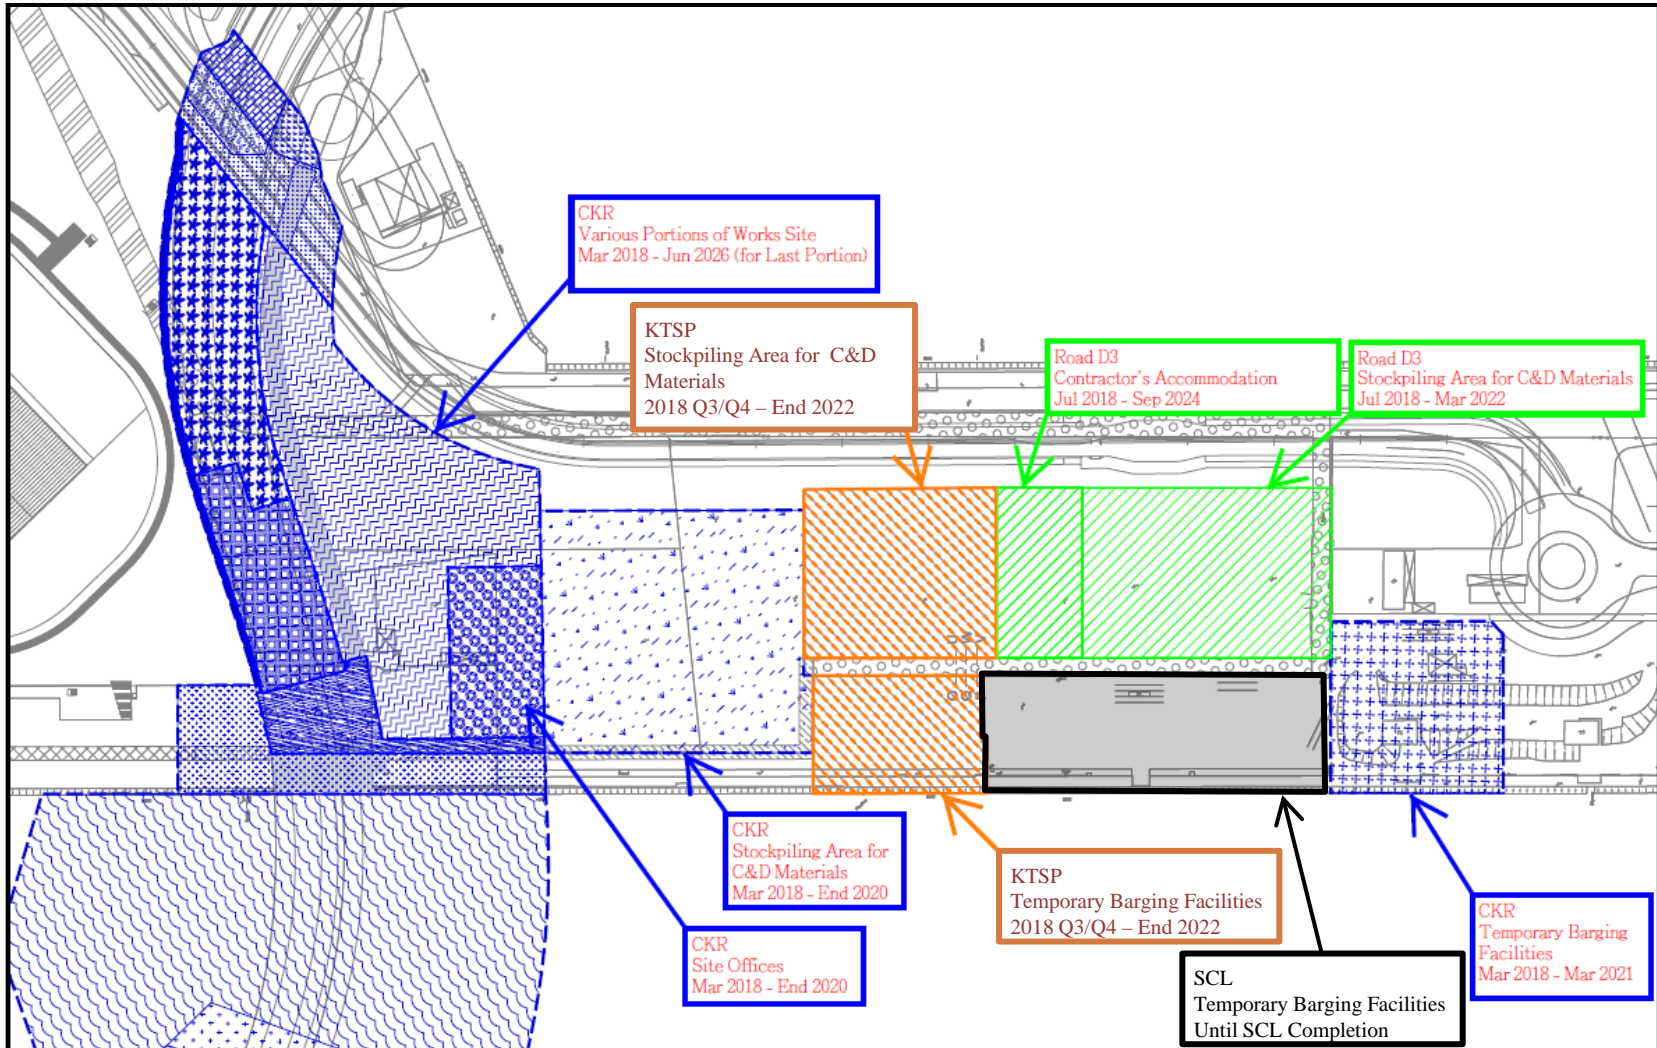

Harbour Enhancement



Graphic hoarding



Screen planting

Harbour Enhancement



Turf Nursery (Singapore Sports Hub)



Existing Fencing



Aesthetic Fencing (samples)

Mitigation Measures



Dust enclosure with sprinkler system

Mitigation Measures



Wheel-washing facility at site entrance



Truck equipped with mechanical cover



Cover temporary stockpile of excavated materials with impervious sheets



香港人的體育公園

Kai Tak Sports Park

A Sports Park for the People of Hong Kong

THANK YOU
